
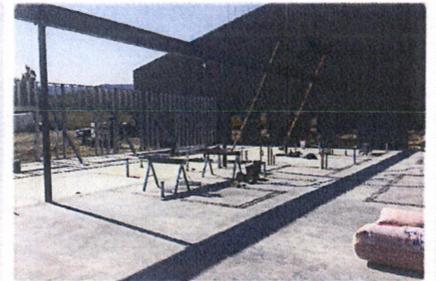


Casper Fire-EMS, Station 6

September 2, 2016

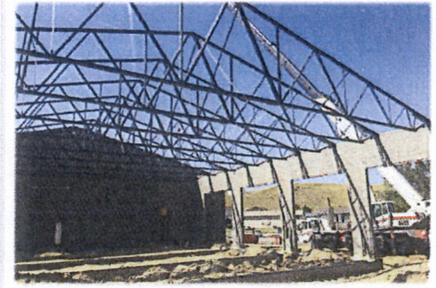

General Field Observations

- Work proceeding according to schedule with exception of propane tank excavations (procurement method/schedule change) and some of the storm drain line extension work.
- Under slab electrical, communications and plumbing rough-ins continue and nearing completion.
- Steel roof trusses in apparatus bay being installed.
- Perimeter, load-bearing metal stud framing has begun.
- Footing and foundation work is near complete.
- Concrete floor slabs have been placed in the living quarters.
